



RICE LIBRARY BUILDING COMMITTEE December 10, 2019

6PM

KITTERY COMMUNITY CENTER

AGENDA

- 1. Project Update
 - a. Design and Construction Schedule
 - b. Subcommittees
 - i. Technology
 - ii. Furniture
 - c. RFQ for Owners Agent
- 2. Design Status (Scott Simons Architects)
 - a. Recap of Schematic Design and Feedback
 - b. Design Development Kick-Off
 - i. Design Development Schedule
 - ii. Working Session
 - c. Review Design Process
 - i. Discuss Action Items
- 3. Next Meeting
 - a. Committee Meeting Schedule Going Forward
 - b. Committee Action Items
 - c. SSA Team Action Items

Materials (also in Drop Box):

- Design and Schedule Update



Rice Public Library

December 2, 2019

MEETING POSTPONED TO DECEMBER 10, 2019



Scott Simons - Principal

Ryan Kanteres - Project Architect



Michael Lassel - Principal


Sarah Hourihane - Project Architect


Curtis Boivin - Architect




Recap of Schematic Design



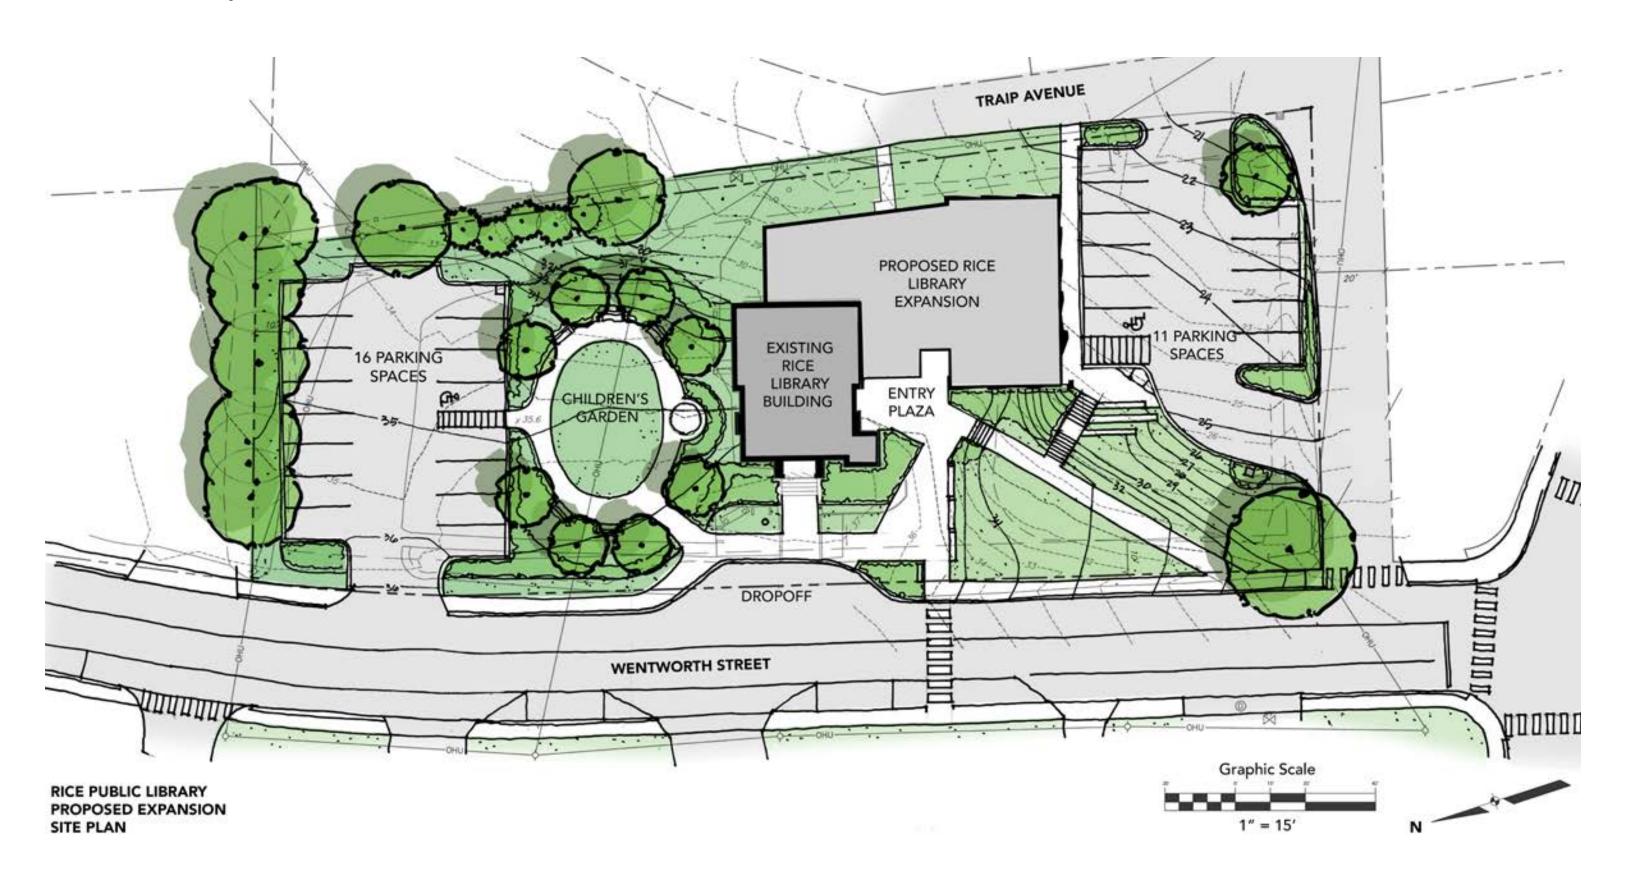

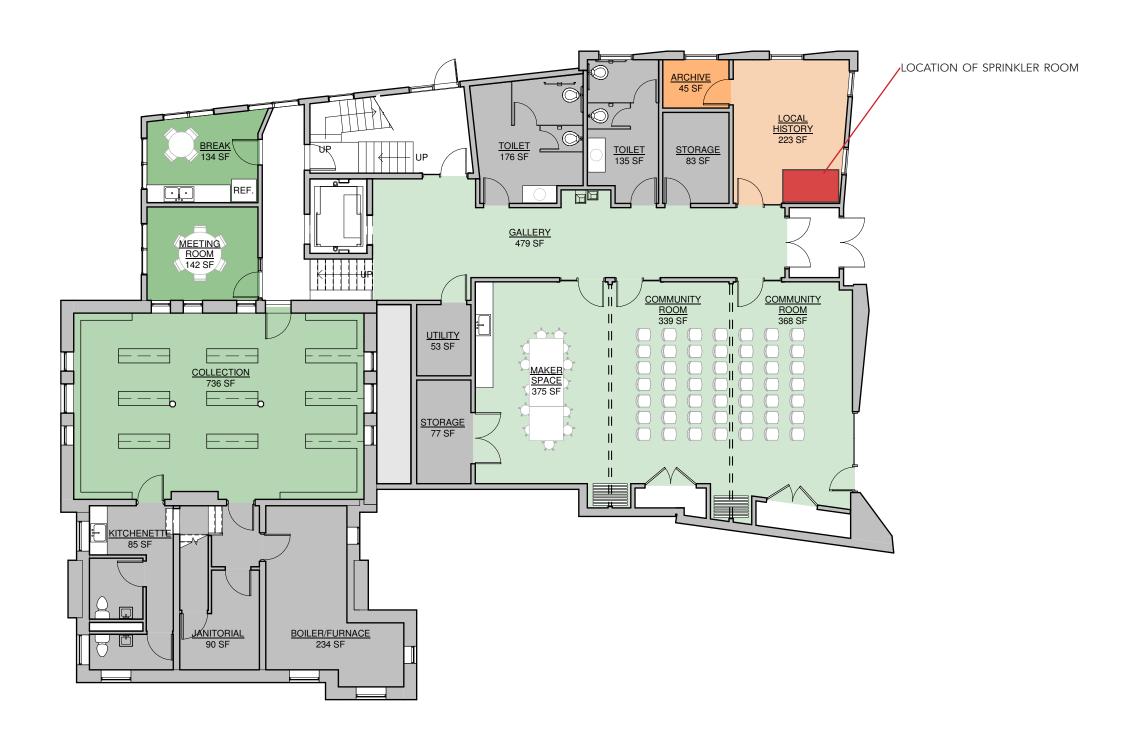

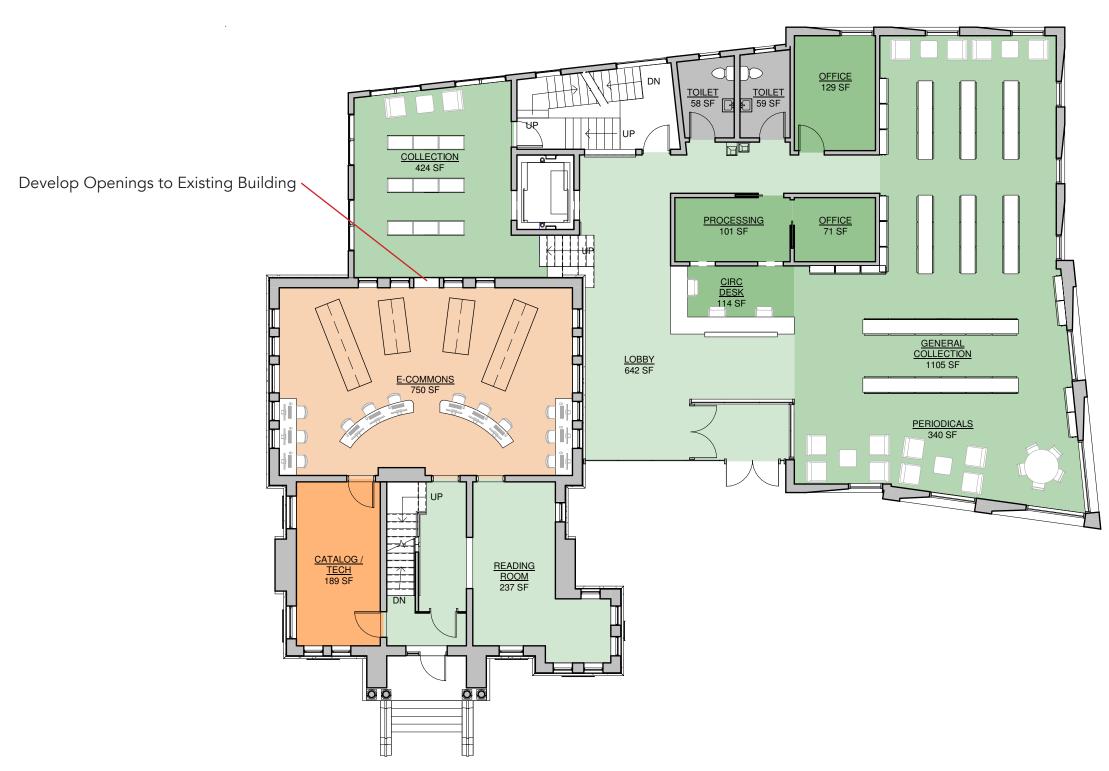






Design Development Kickoff

ScottSimons**Architects**


Rice Public Library													Des	ign																				(Constr	ucti	on								
Updated November 26, 2019	Now			Оес				Ja				Feb			Mar					pril		ı	Vlay			Jui					July			August	September	October	November	January	February	March	April	June	July	August	
Week Beginning	11	18	25	2	9	16 2	3 3	31 (6 13	20	27	3	10 17	7 24	1 2	9	16	23 3	0	5 12	19	26	4 '	11 1	8 25	5 1	8	15	22	29	6	13 2	20 27	7											I
																																						上							floor
Meetings with the Building Committee				\blacktriangle			4	\					A					A					\blacktriangle															Ш.						丄	⊥
Planning Board Approvals																																													L
Pre-application meeting																																													L
Submit Application																																						Ш.						丄	┸
Alt Planning Board Meeting (12/19-1/9, 1/9-1/23, 2/13-2/27)								A	.					A																															
Board of Appeals (12/24 - 1/14)									A																																				1
																																													T
Planning Board Meeting (1/3 - 1/23, 2/6 - 2/27)														A																															Ī
State Fire Marshal Review																									-	1 2	3	4	5	6	7														
Design Development Phase (12 Weeks)				1	2	3	4	5 6	6 7	8	9	10	11 12	2																															I
DD Kickoff (Dec 3)				lack																																									
Issue DD set for Pricing and Coordination (Feb 17)																																													
Owner Review																																						丄						╧	┸
Cost Estimate																																						丄						╧	╧
Construction Documents Phase (12 Weeks)																1	2	3	4	5 6	7	8	9	10 1	1 12	2												丄						丄	┸
Issue 50% Coordination+ Owner Review Set																				A																									퇶
75% pricing																						\blacktriangle																							Ţ
Issue Final Coordination Set																							4	A																					퇶
Internal QA/QC Review																																												\bot	퇶
Complete Bid Set (May 25)																																												\bot	퇶
Bidding Phase (4 Weeks) could be reduced		\sqcup								$\downarrow \downarrow \downarrow$	\Box												_	\perp		1	2	3	4					1				Щ						\bot	\downarrow
Signed Contract (Jun 29)		$\sqcup \bot$								$\downarrow \downarrow \downarrow$								_								_		<u> </u>	Ш					1				4	igspace					\bot	Ŧ
Submit for Building Permits (Jun 29)		\sqcup								$\downarrow \downarrow \downarrow$													_	\perp		1		<u> </u>	Ш									Щ							ļ
Construction Phase (14 months)		$\sqcup \bot$								$\downarrow \downarrow \downarrow$				_												1							1 1	1	2	3	4	5 6	7	8	9 1	0 1	1 12	2	1
Start Construction: (July 20, 2020)																																4	A					\bot						\bot	↓
Construction Complete: (July 20, 2021)																																													
																																													T


Rice Public Library	Design Nov Dec Jan Feb Mar																	
Updated November 26, 2019 Week Beginning		7		Dec	;				Jan				Feb				Mar	
Week Beginning	11	18	25	2	9	16	23	31	6	13	20	27	3	10	17	24	2	9
Meetings with the Building Committee																		
Planning Board Approvals																		
Pre-application meeting																		
Submit Application																		
Alt Planning Board Meeting (12/19-1/9, 1/9-1/23, 2/13-2/27)																		
Board of Appeals (12/24 - 1/14)																		
Planning Board Meeting (1/3 - 1/23, 2/6 - 2/27)																		
State Fire Marshal Review																		
Design Development Phase (12 Weeks)				1	2	3	4	5	6	7	8	9	10	11	12			
DD Kickoff (Dec 3)																		
Issue DD set for Pricing and Coordination (Feb 17)																		
Owner Review																		
DD Cost Estimate																		
Complete HVAC comfort survey						A												
Exterior Material Selection																		
Finish Selections (Major only)																		
Finish Selections (Additional items)																		
Plumbing Fixtures																		
Lighting Selections																		
Shelving Furniture Inventory																		
Circulation Desk																		
Landscape Selections																		
Tech and Security (First Draft)																		



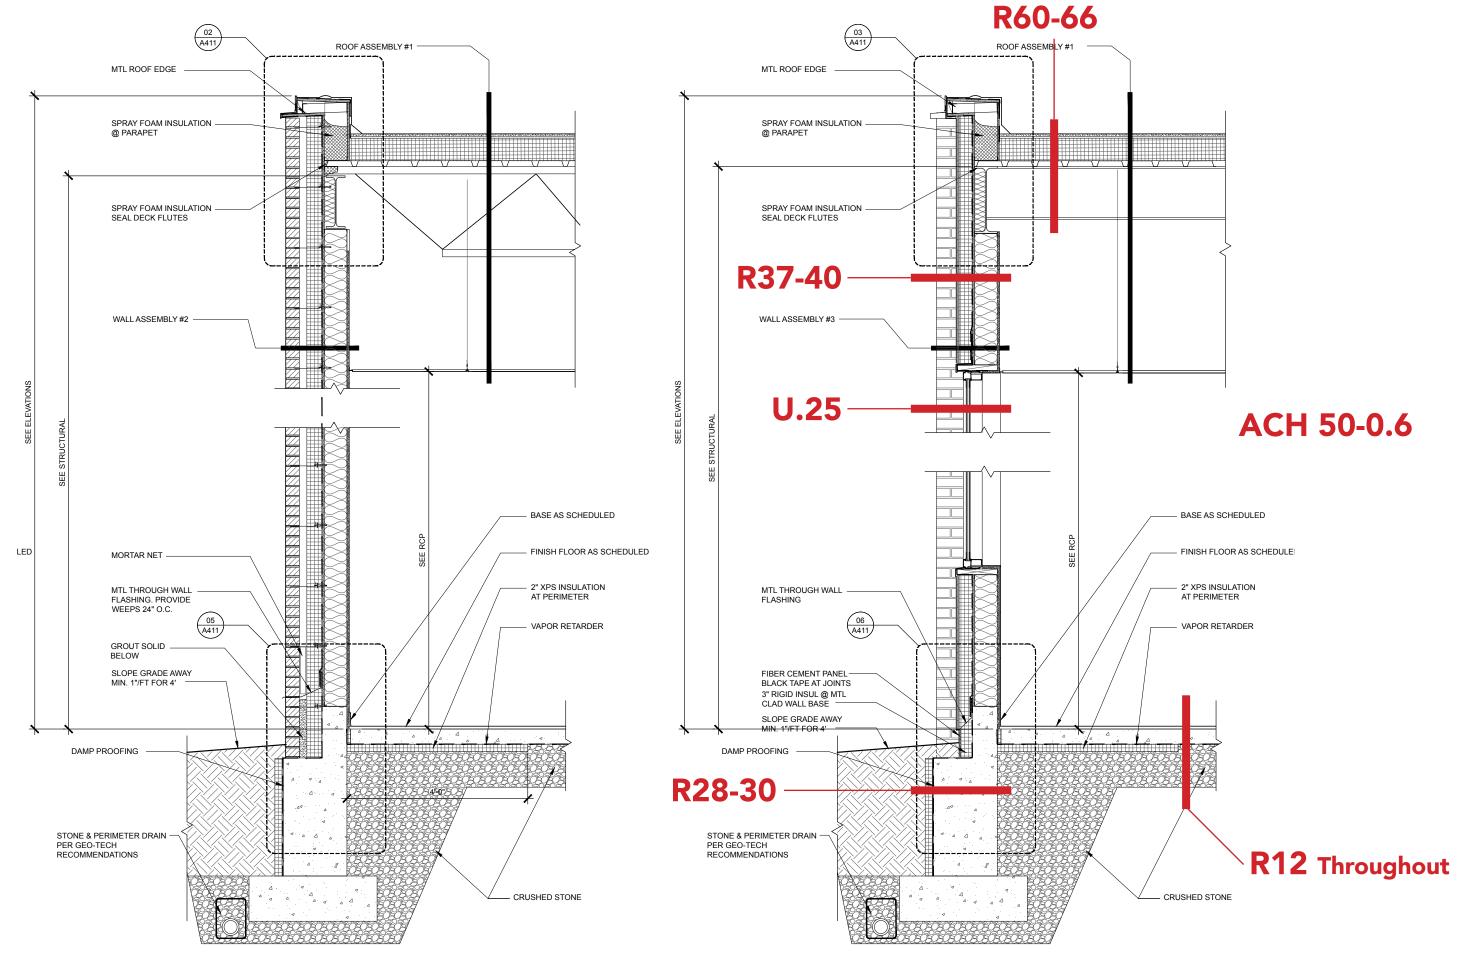


Building Assemblies

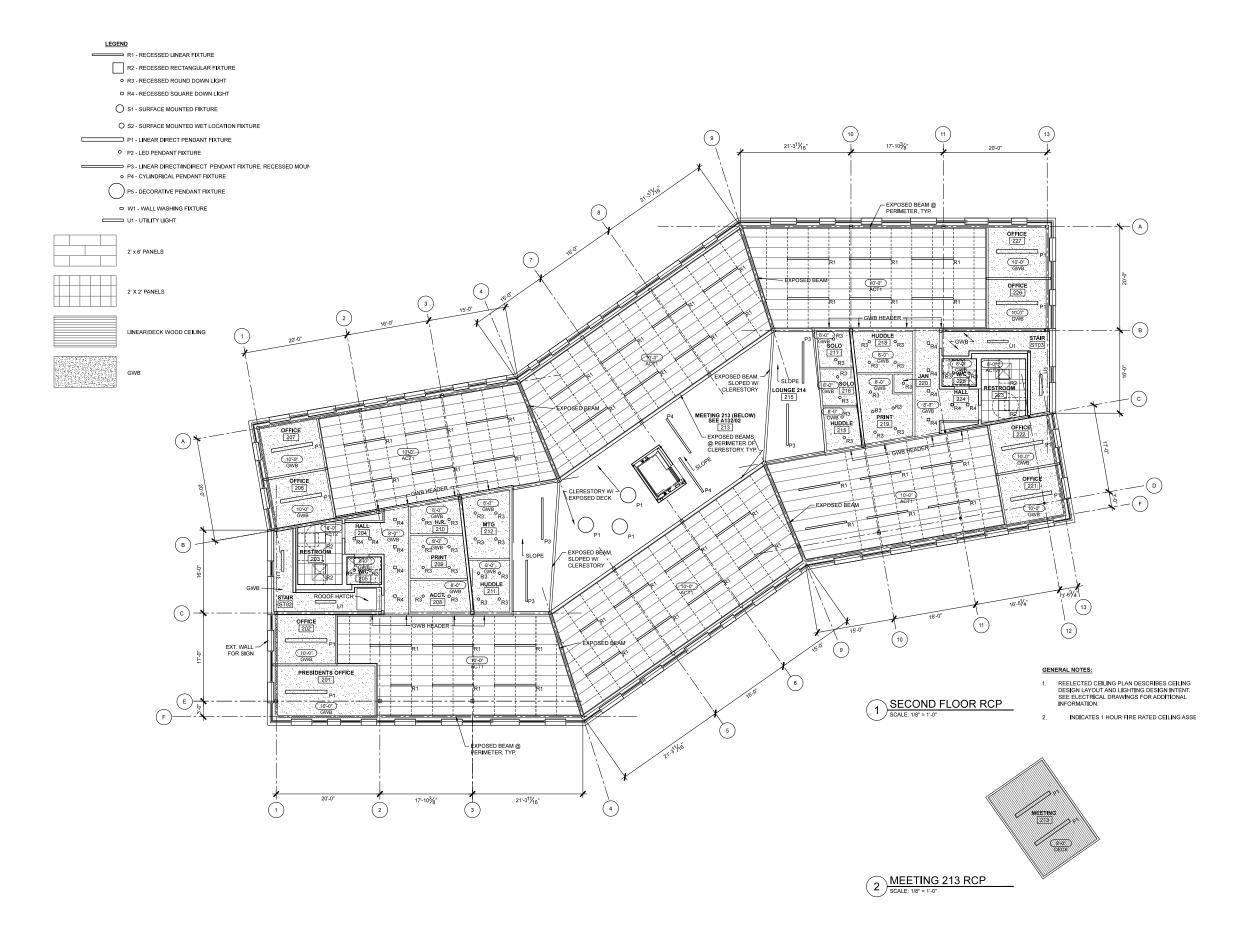

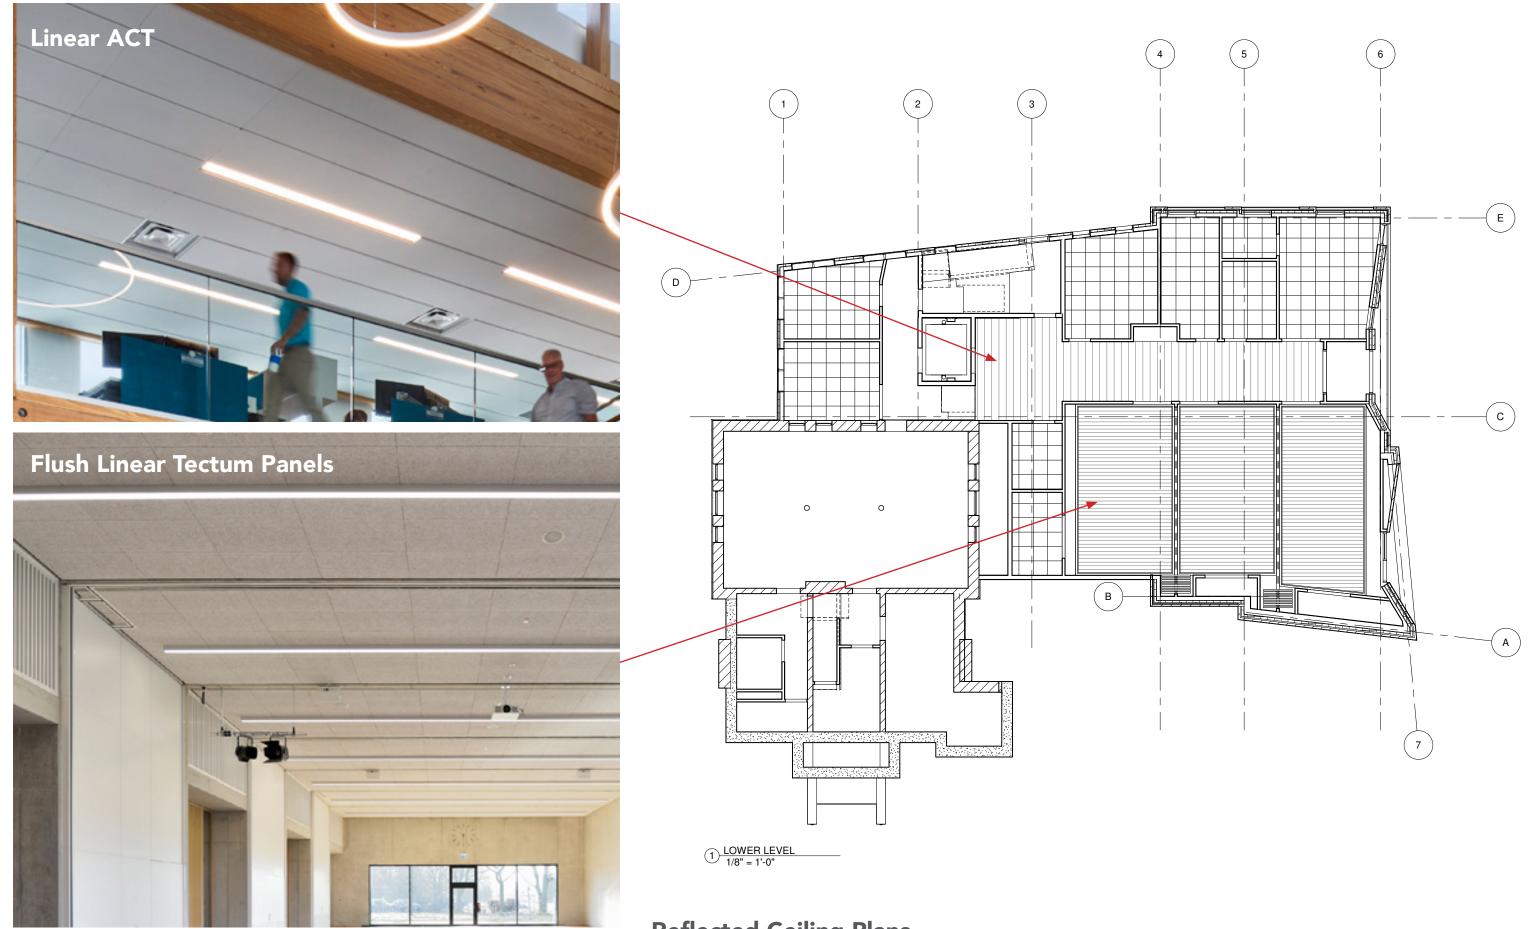

Reflected Ceiling Plans








R2 Recessed Rectangular



R3 Recessed Down Round




R4 Recessed Down Square




P3 Pendant



P4 Pendant

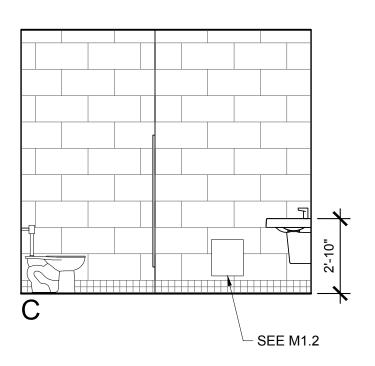

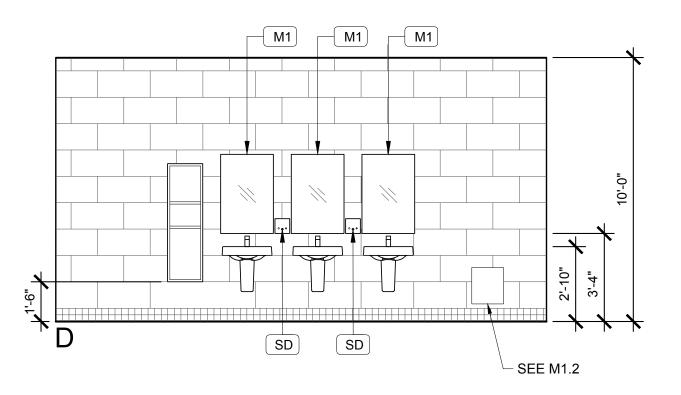





P1 Wall Hung Toilet with automatic flush control



P2 Floor Mounted Toilet with automatic flush control



P3 Wall Mounted Urinal



P4 Wall Hung Lavatory Rectangular



P5 Drinking Fountain



PA Recessed bottle filling station

Plumbing Fixture Direction:

Wall Mounted Toilets vs. Floor Mounted:

- -Floor mounted easier to install less infrastructure
- -Wall mounted are easier to clean around
- -Wall mounted infrastructure reduces room size

Bottle Filling Station vs. Gooseneck Filler



Recessed Paper Towel and Trash Dispenser (ADA Compliant)



Dyson Airblade V Hand Dryer

Wall Mounted Bobrick

Soap Dispenser





Wall Mounted Bobrick Automatic Soap Dispenser





0 0


Recessed Bobrick Automatic Soap Dispenser

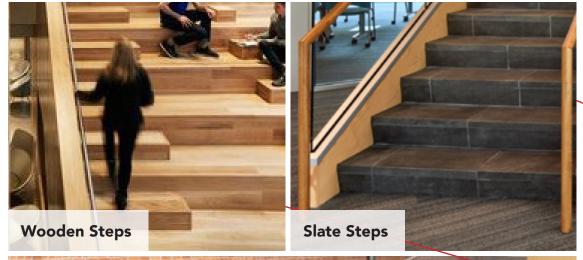

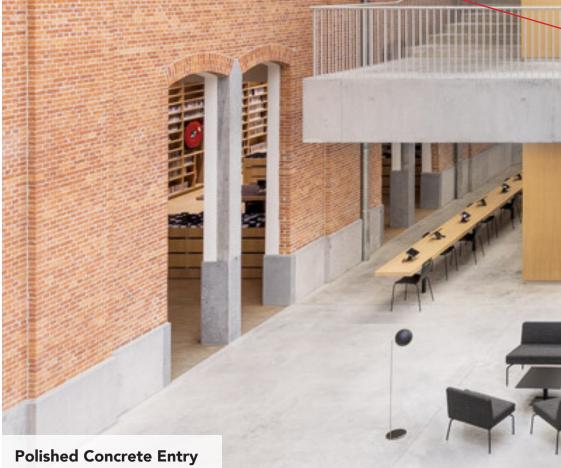



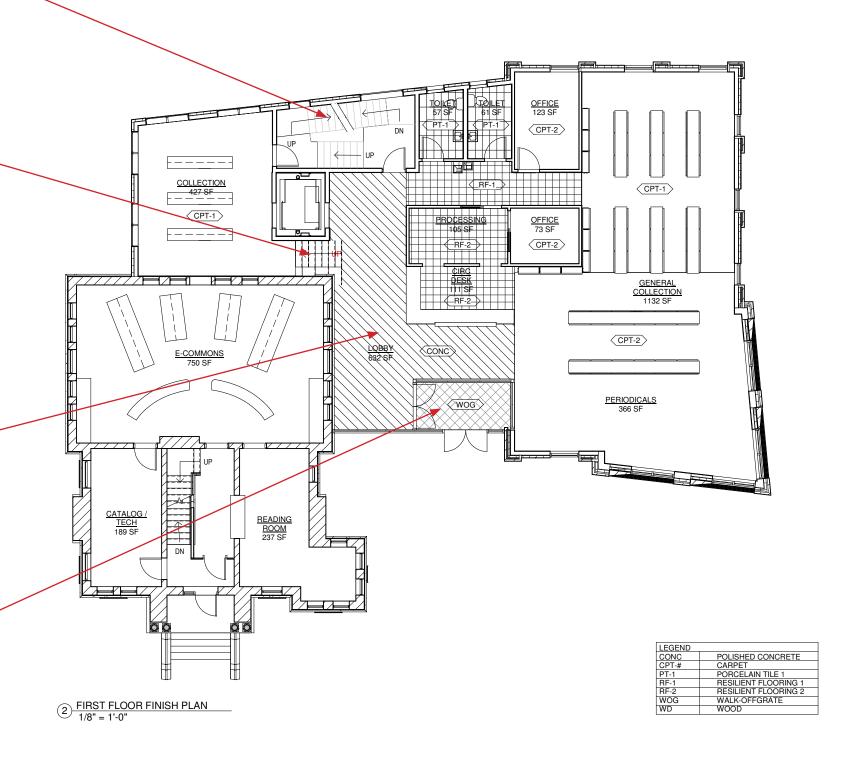

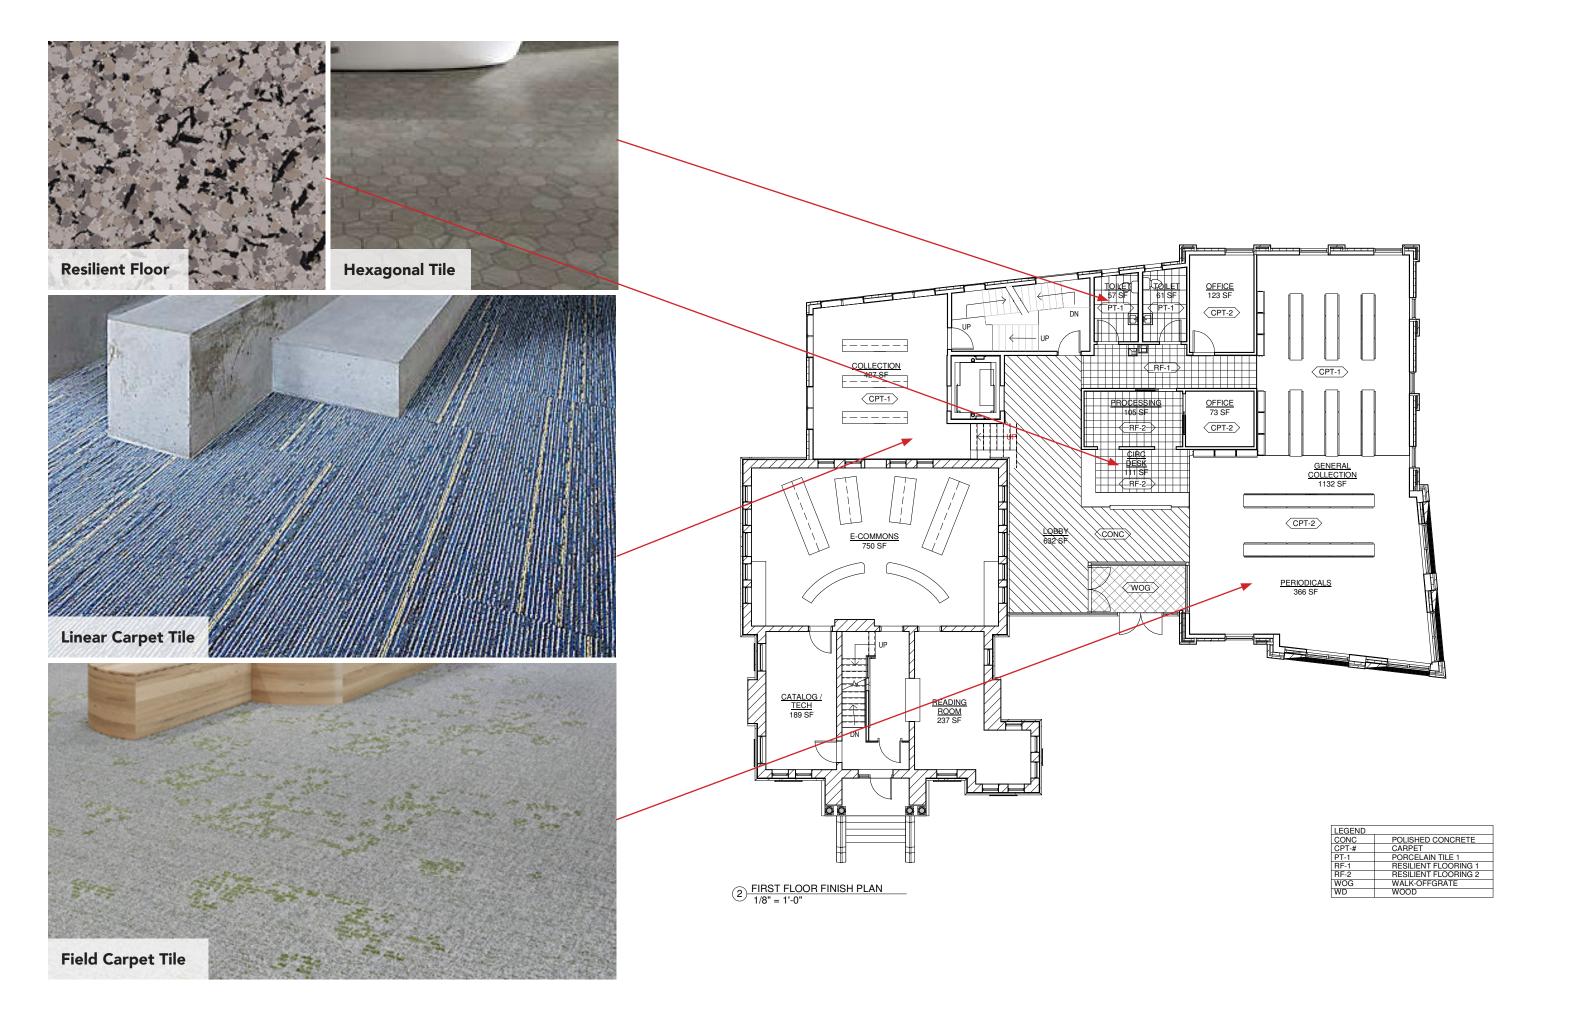



Design Progress

