Proposed Construction Schedule

Pepperell Road Drainage Improvements
In the town of **Kittery**

ID	Task Name	Duration	Start	Finish
1	MOBILIZE, SIGNS & SAW CUTTING	1 day	Wed 12/12/12	Wed 12/12/12
2	BEGIN DRAINAGE AND PREP FOR PIPE BURSTING	1 day	Thu 12/13/12	Thu 12/13/12
3	PIPE BURSTING	1 day	Fri 12/14/12	Fri 12/14/12
4	DRAINAGE	4 days	Mon 12/17/12	Thu 12/20/12
5	RESTORATION	1 day	Fri 12/21/12	Fri 12/21/12

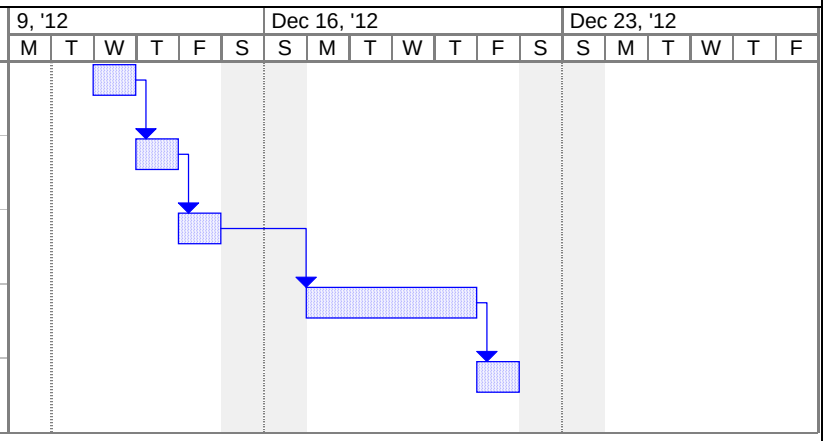

DATE: Tue 12/11/12
REVISION NO.: Original

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
